

KEY POINTS



Approx 175 tonnes of scaffold built in the chamber in 12 days built around all existing fixtures fittings furniture, existing lights, beams, steel ties, glass panels and fingers.

8 DAYS

175 Tonnes removed in 8 days around the same fixtures and fittings new bespoke lights, TV's etc.

175 Tonnes transported in and out by hand from Members Garden to Debating Chamber



51

Window film applied to internal screens below louvres

36 LED

Linear lights all dimmable and individually controlled from a hand held iPad

50%

Of the oak ceiling removed and replaced

New vertical and horizontal motorised blinds had fabric replaced and motors installed with latest low noise models

24

11

New CHS stainless steel beams fitted to high level beams

52

Individually bespoke oak and perspex louvres fitted to west elevation glass screen

75

Down lights

82 LED

Spotlights



83

Roof-lights above louvres (by rope access)


41 LED

Bespoke suspended lights weighing in excess of 30kg each

+ ZERO

Injuries and ill health incidents

MAN HOURS

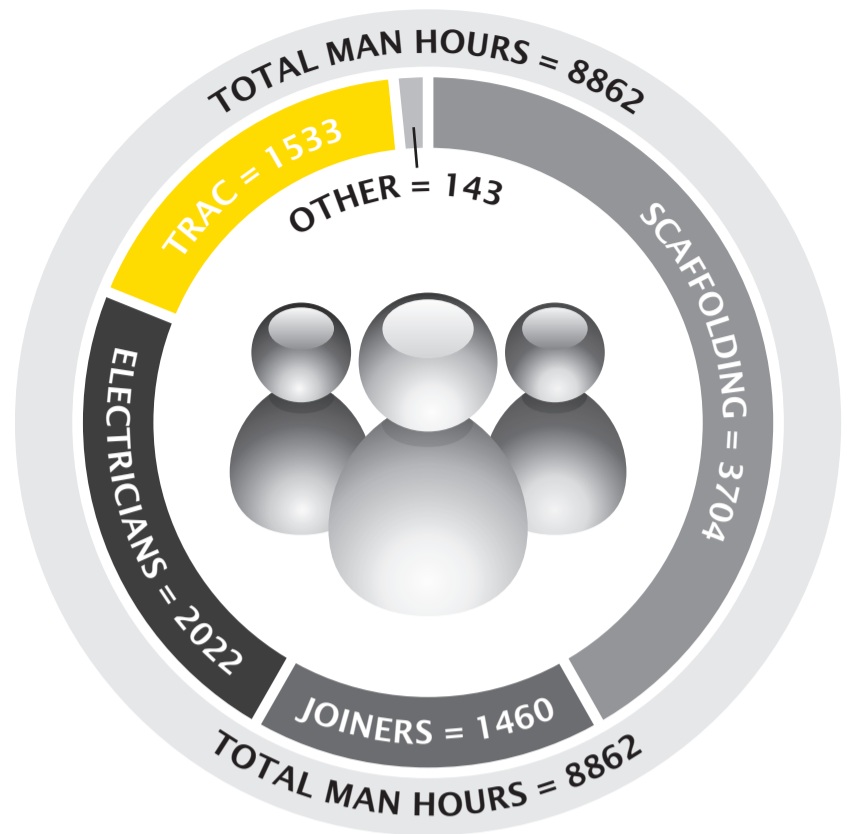

INDUCTED PERSONNEL

	PRINCIPAL DESIGNER	2
	PRINCIPAL CONTRACTOR	18
	CLIENT	8
	SCAFFOLDERS	34
	JOINERS	16
	BLINDS	5
	LIGHTING	7
	ELECTRICAL	14
	OTHER	4

TOTAL 108
